


II – 8. Framework scaffolding (base section)

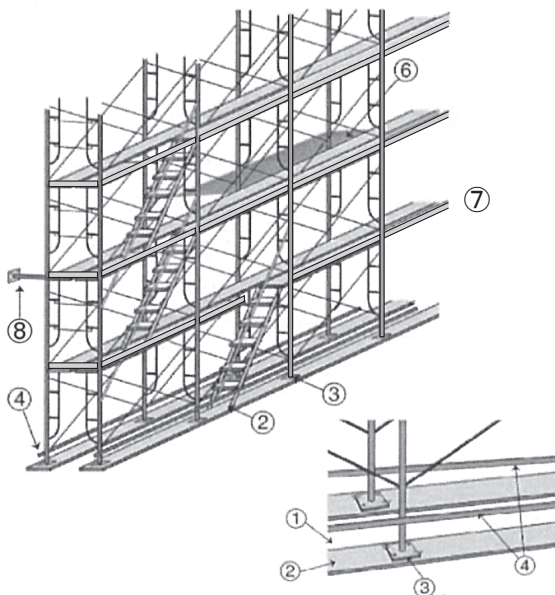

1. Has the ground surface been compacted?
2. Have baseplates been used?
3. Have jack bases been secured to the sill with nails?
4. Are the lower parts of standards connected with ledger pipes?
5. Is the space between the scaffolding and the building no more than 30 cm?
6. Has horizontal netting been installed where gaps exceed 30 cm?
7. Have braces been installed throughout the scaffolding?
8. Have wall ties been properly installed?
